

#### **CABONNE COUNCIL**

# CONTRACT No. 1160872 LUMP SUM CONTRACT

for the

# INSTALLATION OF CULVERTS AND SUPPLY & INSTALL FOOTPATHS, KERB & GUTTERING IN THE CABONNE COUNCIL LGA

PREPARED BY:
COUNCIL'S DEPARTMENT OF
TRANSPORT INFRASTRUCTURE
DATE: SEPTEMBER 2020



**CABONNE COUNCIL** 

# CONTRACT No. 1160872 LUMP SUM CONTRACT

for the

# INSTALLATION OF CULVERTS AND SUPPLY & INSTALL FOOTPATHS, KERB & GUTTERING IN THE CABONNE COUNCIL LGA

### INFORMATION FOR TENDERERS

PREPARED BY:
COUNCIL'S DEPARTMENT OF
TRANSPORT INFRASTRUCTURE
DATE: SEPTEMBER 2020

#### **CONTENTS**

|   |  | AGE |
|---|--|-----|
| 1 | PROJECT IDENTIFICATION AND DESCRIPTION | 1   |
| 2 | RELEVANT DOCUMENTS                     | 2   |
| 3 | TENDERING METHOD                       | 2   |
| 4 | COUNCIL'S CONTACT PERSON               | 2   |
| 5 | SITE INSPECTION                        | 2   |
| 6 | TENDER LODGEMENT REQUIREMENTS          | 3   |

#### **INFORMATION FOR TENDERERS**


#### **GENERAL**

#### 1 PROJECT IDENTIFICATION AND DESCRIPTION

This tender is for Contract No. 1160872 Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA.

This is a Lump Sum Contract.

#### **LOCATION PLAN**

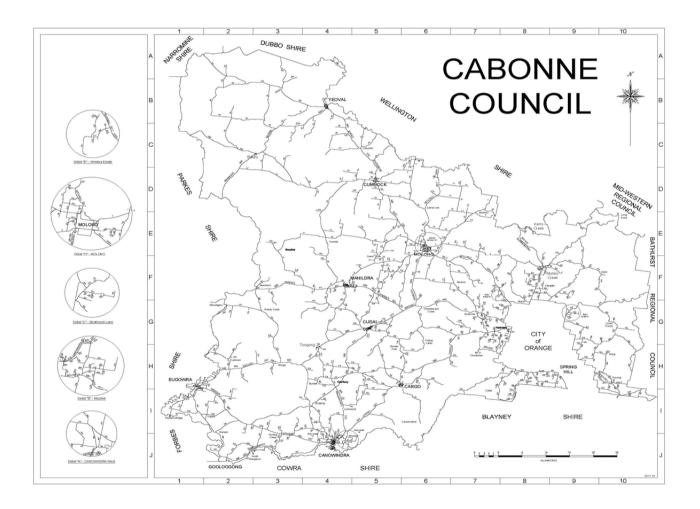

© IPWEA 2004 1 CABONNE COUNCIL

#### Contract No. 1160872

#### 2 RELEVANT DOCUMENTS

- (a) The Contract Documents for this project are:
- General Conditions of Contract (AS 4000-1997) \*
- Specifications
- Drawings
- Tender Submission Forms
- \* AS 4000-1997 is not included as part of the contract documentation. Copies are available from Standards Australia
- (b) The following documentation is provided for the information of the Tenderers and does not form part of the Contract Documents:
- Information for Tenderers and Conditions of Tendering

The documents are available from Council's Engineering and Technical Services Department, Main Street, Cudal, Council's website <a href="www.cabonne.nsw.gov.au">www.cabonne.nsw.gov.au</a> and Council's E- tendering website <a href="www.tenderlink.com/cabonne">www.tenderlink.com/cabonne</a>.

The Tenderer warrants and represents that it will, prior to submission of tender, obtain the information and documentation referred to above and will obtain all other information relevant to the works, contingencies and other circumstances having an effect on its tender.

#### 3 TENDERING METHOD

This Contract shall follow the "The Procedures of Open Tendering" in accordance with AS4120-1994 Clause 6.2.3(b), The Principal invites the public advertisement without restriction on the numbers of tenders sought.

#### 4 COUNCIL'S CONTACT PERSON

Enquiries regarding this tender may be directed to:

Name: Tony Weekes Phone: 02 6390 7100

Position: Department Leader – Transport Infrastructure

#### 5 SITE INSPECTION

Tenderers are not required to attend a site meeting as part of this Tender. It is advisable however that prospective Tenderers visit Cabonne Council LGA and discuss the project requirement with Council. By submitting a tender, it is assumed the Tenderer has visited the site and understands all that is required under this Specification.

© IPWEA 2004 2 CABONNE COUNCIL

#### 6 TENDER LODGEMENT REQUIREMENTS

Tenders shall be submitted on the Tender Forms provided by the Principal, Tender Submission Documents, and are to be enclosed in a sealed envelope and the envelope marked legibly as follows:

Contract No. 1160872

Tender for Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering

in the Cabonne Council LGA

and either:

delivered by hand or by courier and placed in the:

Tender Box Cabonne Council 97 Bank Street MOLONG NSW 2866

or

mailed to the Tender Box addressed as follows, and marked:

"Contract 1160872 Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA"

Tender Box Cabonne Council PO BOX 17 MOLONG NSW 2866

or

submitted electronically on

www.tenderlink.com/cabonne

so as to be received before the closing time and date for tenders.

Time: 12:00 pm, noon

Date: Wednesday, 14 October 2020

© IPWEA 2004 3 CABONNE COUNCIL



**CABONNE COUNCIL** 

# CONTRACT No. 1160872 LUMP SUM CONTRACT

for the

# INSTALLATION OF CULVERTS AND SUPPLY & INSTALL FOOTPATHS, KERB & GUTTERING IN THE CABONNE COUNCIL LGA

### **CONDITIONS OF TENDERING**

PREPARED BY:
COUNCIL'S DEPARTMENT OF
TRANSPORT INFRASTRUCTURE
DATE: SEPTEMBER 2020

#### **CONTENTS**

| CLAU | JSE                                   | PAGE |
|------|---------------------------------------|------|
| GEN  | NERAL                                 | 1    |
| 1.   | PREAMBLE                              | 1    |
| 2.   | PROJECT INFORMATION                   | 1    |
| 3    | RELEVANT DOCUMENTS                    | 1    |
| 4    | CONTRACTOR'S RESPONSIBILITY           | 2    |
| 5    | COUNCIL'S CONTACT PERSON              | 2    |
| TEN  | IDER SUBMISSION INFORMATION           | 2    |
| 6    | SUPPORTING INFORMATION FROM TENDERERS | 2    |
| 7    | SUBCONTRACTORS                        | 2    |
| 8    | SITE INSPECTION                       | 2    |
| 9    | ALTERNATIVE PROPOSALS                 | 2    |
| 10   | TENDER VALIDITY PERIOD                | 3    |
| 11   | TENDER LODGEMENT REQUIREMENTS         | 3    |
| 12   | LATE TENDERS                          | 3    |
| 13   | TENDER EVALUATION AND SELECTION       | 3    |
| 14   | POST TENDER SUBMISSIONS               | 4    |
| 15   | POST TENDER NEGOTIATIONS              | 4    |
| 16   | COST OF TENDERING                     | 4    |
| 17   | CONTRACT COMMENCEMENT DATE            | 4    |

#### **CONDITIONS OF TENDERING**

#### **GENERAL**

#### 1. PREAMBLE

Contract No: 1160872

The Conditions of Tendering have been prepared in accordance with the obligations of the Principal contained in the Australian Standard 4120-1994, Code of Tendering, which sets out the ethics and obligations of the Principal and Tenderers in tendering in the construction industry.

Tenderers and Principal shall comply with the requirements of this AS 4120-1994. In particular attention is drawn to the obligations of Tenderers, in the preparation and submission of their tender for this project.

Without limiting the above obligations: -

- · Tenderers shall not submit tenders without a firm intention to proceed.
- Tenderers must not engage in any form of collusive practice.
- Any Tenderer who directly or indirectly canvasses support from an elected member or servant of the Council will be disqualified.

It should be noted that in all contract documentation words importing a gender include every gender.

#### 2. PROJECT INFORMATION

The complete project description, scope of work, specific site and project requirements shall be as defined in the Specification.

This tender is for Contract No. 1160872 Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering and the Installation of Culverts in the Cabonne Council LGA.

It is a Lump Sum Contract.

#### 3 RELEVANT DOCUMENTS

(a) The contract documents for this project are:

#### **CONDITIONS OF CONTRACT**

- General Conditions of Contract (AS 4000-1997) \*.
- Annexures to General Conditions of Contract.
- \* AS 4000-1997 is not included as part of the contract documentation. Copies are available from Standards Australia.

#### **TENDER SUBMISSION FORMS**

**SPECIFICATIONS** 

**DRAWINGS** 

© IPWEA 2004 1 CABONNE COUNCIL

#### 4 CONTRACTOR'S RESPONSIBILITY

Contract No: 1160872

It shall be the responsibility of the Contractor to ascertain all information relating to the services, the works and site conditions that may affect the progress or method of performing all services and works as specified within the scope of this contract and to prepare for every contingency that may arise. It is further understood that just provision for these contingencies have been accounted for, implicitly or explicitly within the Bill of Quantities or Schedule of Rates submitted.

#### 5 COUNCIL'S CONTACT PERSON

Enquiries regarding this tender may be directed to:

Name: Tony Weekes Phone: 02 6390 7100

Position: Department Leader – Transport Infrastructure

#### TENDER SUBMISSION INFORMATION

#### **6 SUPPORTING INFORMATION FROM TENDERERS**

The Tenderer shall provide documentary evidence to prove they have the necessary competence, resources, industrial relations, quality and safety management and financial capacity to carry out the Works.

- Copy of Certificate of Currency for Public Liability Insurance
- Copy of Work Health & Safety (WHS) Management Plan
- Copy of Environmental Management Plan
- Copy of Quality Management Plan
- Copy of Safe Work Method Statement (SWMS)

#### 7 SUBCONTRACTORS

The Tenderer is required to provide, on the tender form in the Tender Submission Documents, the names and telephone numbers of Tenderer's Subcontractors and recognise by initials the Principal's listing of Selected and Nominated Contractors.

#### 8 SITE INSPECTION

Tenderers are not required to attend a site meeting as part of this Tender. It is advisable however that prospective Tenderers visit Cabonne Council LGA and discuss the project requirement with Council. By submitting a tender, it is assumed the Tenderer has visited the site and understands the all that is required under this Specification.

#### 9 ALTERNATIVE PROPOSALS

Alternative proposals, which satisfy the Principal's basic commercial and performance objectives, technical and legal requirements, may be submitted as options but only in addition to a conforming tender. All costs associated with the design and documentation of any alternative proposal shall be borne by the Tenderer.

© IPWEA 2004 2 CABONNE COUNCIL

#### 10 TENDER VALIDITY PERIOD

Contract No: 1160872

Tenders will be valid for a period of 60 days from the tender closing date. In the event of the withdrawal of the tender prior to the expiration of this period, the Tenderer shall be liable for all costs, losses or damages suffered by the Principal by reason of that withdrawal.

#### 11 TENDER LODGEMENT REQUIREMENTS

Tenders shall be submitted on the forms provided by the Principal in the Tender Submission Documents, and are to be enclosed in a sealed envelope and the envelope marked legibly as follows:

Contract No. 1160872

Tender for Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering

in the Cabonne Council LGA

and either:

delivered by hand or by courier and placed in the:

Tender Box Cabonne Council Bank Street MOLONG NSW 2866

or

mailed to the Tender Box addressed as follows, and marked

"Contract No 1160872 Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA"

Tender Box Cabonne Council PO BOX 17 MOLONG NSW 2866

or

submitted electronically on <u>www.tenderlink.com/cabonne</u>

so as to be received before the closing time and date for tenders.

Time: 12:00 noon

Date: Wednesday, 14 October 2020

#### 12 LATE TENDERS

A tender which is received after the closing time and date will only be considered if the Tenderer can satisfy Council that it complies with Clause 177 (5) of the Local Government (General) Regulations 2005.

#### 13 TENDER EVALUATION AND SELECTION

Evaluation, negotiation and selection of tenders shall be in accordance with the requirements of AS 4120 (1994), Code of Tendering and Local Government Regulations 2005 under the Local Government Act 1993.

The evaluation criteria shall be:

Lump sum tender amount

© IPWEA 2004 3 CABONNE COUNCIL

- Contract No: 1160872
- Evidence of technical and financial capability
- Industry reputation and past record of providing similar services
- Quality Management Plan, Work Health and Safety Management Plan and Environmental Management Plan

The Principal is not bound to accept the lowest, or any tender.

The successful Tenderer which is accepted shall be notified in writing to all Tenderers.

#### 14 POST TENDER SUBMISSIONS

The Principal may call for post tender submissions from some or all tenderers in order to assist with the evaluation.

Such submissions will be confidential between the Principal and Tenderer.

The call for such submissions will not bind the Principal to proceed to accept a tender.

#### 15 POST TENDER NEGOTIATIONS

The Principal may enter into negotiation with a Preferred Tenderer or a number of candidate tenderers.

Such negotiations will be confidential between the Principal and Tenderer and will be conducted in accordance with guidelines set out in AS 4120 (1994).

The undertaking of negotiations will not bind the Principal to proceed to accept a tender.

#### 16 COST OF TENDERING

All costs associated with tender preparation and submission shall be borne by the Tenderer.

#### 17 CONTRACT COMMENCEMENT DATE

The commencement of the Contract is nominated as the date of instrument of agreement between Council and the successful Tenderer. There shall be no Contract prior to the issue of a letter of acceptance and a signed Instrument of Agreement.

© IPWEA 2004 4 CABONNE COUNCIL



#### **CABONNE COUNCIL**

### **CONTRACT No. 1160872**

#### **LUMP SUM CONTRACT**

for the

# INSTALLATION OF CULVERTS AND SUPPLY & INSTALL FOOTPATHS, KERB & GUTTERING IN THE CABONNE COUNCIL LGA

## **CONDITIONS OF CONTRACT**

PREPARED BY:
COUNCIL'S DEPARTMENT OF
TRANSPORT INFRASTRUCTURE
DATE: SEPTEMBER 2020

## **CONTENTS**

- 1. GENERAL CONDITIONS OF CONTRACT
- 2. ANNEXURES TO THE GENERAL CONDITIONS OF CONTRACT
  - PART A
  - PART B
  - PART C

# GENERAL CONDITIONS OF CONTRACT

© IPWEA 2004 Page 2

CABONNE COUNCIL

# THE GENERAL CONDITIONS OF CONTRACT SHALL BE

# AUSTRALIAN STANDARD (AS) 4000 - 1997 THIS DOCUMENT IS DEEMED TO BE INCLUDED IN THE CONTRACT DOCUMENTS

Copies are available from Standards Australia. Copies may be viewed at Cabonne Council's Cudal office by appointment with the Contact Officer nominated in the Conditions of Tendering.

# **ANNEXURE**

to the

# GENERAL CONDITIONS OF CONTRACT

#### **ANNEXURE to the Australian Standard General Conditions of Contract AS4000-**1997

## PART A -

This Annexure shall be completed and issued as part of the tender documents and, subject to any amendments to be incorporated into the Contact, is to be attached to the General Conditions of Contract and shall be read as part of the Contract.

| Item |  |   |
|------|--|---|
| 1    | Principal<br>(clause 1)                            | CABONNE COUNCIL   |
|      |  | ABN: <b>41 992 919 200</b>  |
| 2    | Principal's address                                | PO Box 17 MOLONG NSW 2866 Ph 6390 7100 Principals Representative: Cabonne Council's Deputy General Manager – Cabonne Infrastructure   |
| 3    | Contractor<br>(clause 1)                           |   |
|      |  | ABN:  |
| 4    | Contractor's address                               |   |
| 5    | Superintendent<br>(clause 1)                       | Cabonne Council's Department Leader – Transport Infrastructure Ph 6390 7100 Superintendent's Representative: Cabonne Council's Contracts Coordinator  |
| 6    | Superintendent's address                           | PO Box 17<br>MOLONG NSW 2866  |
| 7    | Period of time for practical completion (clause 1) | The works under the contract are for the fiscal year 2020-21. The works may be spread over the Council area. The time for practical completion of the works at each site will be negotiated at the time of acceptance of the offer. |
| 8    | Governing law:<br>(page 5, clause 1(h))            | New South Wales   |
| 9    | (a) Currency (page 5, clause 1(g))                 | Australian Dollars  |

(b) Place of payments (page 5, clause 1(g))

PO Box 17 MOLONG NSW 2866

(c) Place of Business of Bank (page 5, clause 1(d))

**MOLONG NSW 2866** 

- 10 Bill of quantities (subclause 2.2)
  - (a) Alternative applying (subclause 2.2)

Alternative 1

(b) If Alternative 2 applies, is the *bill* of *quantities* to be priced: (subclause 2.2)

N/A

(c) Lodgement time (subclause 2.3(b))

- At the time of Tender Submission
- 11 Quantities in *schedule of rates*, limits of accuracy (Clause 2.5(b))

N/A

12 *Provisional sum*, percentage for profit and attendance (clause 3)

As assessed by the Superintendent

- 13 Contractor's Security
  - (a) Form (clause 5)
  - (b) Amount or maximum percentage value of this *contract sum* (clause 5)
  - (c) If retention moneys, percentage of each progress certificate applicable to this contract sum (clause 5 and subclause 37.2)
  - (d) Time for provision (except for retention moneys) (clause 5)
  - (e) Additional *security* for unfixed plant and materials (subclauses 5.4 and 37.3)
  - (f) Contractor's security upon certificate of practical completion is reduced by (subclause 5.4)

#### **Retention Money**

5%

If nothing stated, 5% of value of this separable portion

10%

If nothing stated, 10%, until the limit in Item 13(b)

14 Days after acceptance of tender
If nothing stated, within 28 days after due date of acceptance of tender

N/A

50 % of amount held If nothing stated, 50% of amount held

© IPWEA 2004 Page 6

CABONNE COUNCIL

| 14 | Principal's s                             | ecurity   |     |  |
|----|---|---|-----|--|
|    | (a) For                                   | m (clause 5)  |     | N/A  |
|    |   | ount or maximum percenta<br>nis separable portion (claus            |     | N/A  |
|    | (c) Tim                                   | e for provision (clause 5)  |     | N/A If nothing stated, within 28 days after date of acceptance of tender |
|    | pra                                       | ncipal's security upon c<br>ctical completion is re<br>oclause 5.4) |     | W/A  |
| 15 | Principal-su<br>(Clause 6.1)              | oplied documents  |     | Contract documents including:  |
| 16 | Time for Sup<br>documents<br>(subclause 8 | perintendent's direction ab   | out | 14 days  |
| 17 | Subcontract<br>(subclause 9               | <i>work</i> requiring approval<br>9.2)                              |     | All Subcontract work   |
| 18 | Novation (subclause 9                     | 9.4)  |     | N/A  |
| 19 | Legislative r                             | equirements   |     |  |
|    |   | e excepted<br>clause 11.1)  |     | N/A  |
|    | ` '                                       | ified <i>WUC</i><br>clause 11.2(a)(ii))                             |     | N/A  |
| 20 | Insurance o<br>(clause 16)                | the Works   |     |  |
|    | (a) Altern                                | native applying   |     | Alternative 1  |

© IPWEA 2004 Page 7

CABONNE COUNCIL

|    | If Alte          | ernative 1 applies   |   |  |  |
|----|------------------|--|---|--|--|
|    | (b)              | Provision for demolition and removal of debris   | NIL   |  |  |
|    | (c)              | Provision for consultant's fees  | NIL   |  |  |
|    | (d)              | Value of materials or things to be supplied by the <i>Principal</i>  | NIL   |  |  |
|    | (e)              | Additional amount or percentage  | NIL   |  |  |
| 21 | Public<br>(claus | c liability insurance<br>e 17)   |   |  |  |
|    | (a)              | Alternative applying   | Alternative 1   |  |  |
|    | If Alte          | ernative 1 applies   |   |  |  |
|    | (b)              | Amount per occurrence shall be not less than   | \$20,000,000  |  |  |
| 22 |                  | for giving possession<br>lause 24.1)   | Date of acceptance of tender  |  |  |
| 23 | which (page      | fying cause of delay. Cause of delay for EOTs will not be granted 3, paragraph (b)(iii) of clause 1 and ause 34.3) | N/A   |  |  |
| 24 | Liquic           | lated Damages, rate (subclause 34.7)   | \$300 per day   |  |  |
| 25 |                  | s for early <i>practical completion</i><br>se 34.8)  | N/A   |  |  |
| 26 |                  | damages, other compensable causes 1, clause 1 and subclause 34.9)  | Nil   |  |  |
| 27 |                  | ets liability period<br>se 35)   | 12 months from the date of practical Completion of the Works Under the Contract |  |  |
| 28 |                  | ess Claims<br>ause 37.1)   | Daga 9  |  |  |

© IPWEA 2004 Page 8

CABONNE COUNCIL

a) Times for progress claims By the fourteenth (14th) day of each month for WUC done to the last day of the previous month 29 Unfixed plant and materials for which payment N/A claims may be made (subclause 37.3) 30 N/A Interest rate on overdue payments (subclause 37.5) 31 Time for Principal to rectify inadequate 14 days possession (subclause 39.7) 32 Arbitration and Expert Determination: (subclause 42.3) (a) Person to nominate an arbitrator or *Expert*. Chairperson for the time being of the Chapter of the Institute of Arbitrators & Mediators Australia in New South Wales Rules 5-18 of the Rules of The Institute of (b) Rules for arbitration: **Arbitrators & Mediators Australia for the Conduct of Commercial Arbitrations** Rules for expert determination: **Guidelines for Expert Determination of the** (c) **Australian Commercial Disputes Centre** 

# **ANNEXURE - PART B**

#### ANNEXURE PART B

#### 1. Deletions

The following clauses have been deleted from the General Conditions in AS4000-1997.

Clause 29.2 Quality Assurance

Clause 34.8 Bonus for Early Practical Completion (optional)

#### 2. Amendments

The following clauses from the General Conditions in AS 4000-1997 have been amended.

#### CLAUSE 1. INTERPRETATION AND CONSTRUCTION OF CONTRACT

The following interpretations shall be included:

Equipment means the goods to be supplied or supplied by the Contractor pursuant to the

Contract;

#### 3. Additions

The following clauses have been added to AS4000-1997:

#### **CLAUSE 29.6. QUALITY REQUIREMENTS**

The Contractor shall:

- (a) Comply with all the quality requirements as provided in the contract documents for all works under the Contract.
- (b) Ensure that each of its Subcontractors and Consultants comply in like manner.
- (c) Demonstrate to the Principal whenever required that all the quality requirements of the contract are being met.

Where inappropriate or inadequate provision of quality supervision by the Contractor or Contractor's Subcontractor results in costs, losses or damages incurred by the Principal or claims by third parties against the Principal for either direct or consequential costs, losses or damages, the Contractor shall be liable for costs, losses or damages associated with any claim including but not limited to administration costs incurred by the Principal in resolving such claim.

#### CLAUSE 44. WORK, HEALTH AND SAFETY (W H & S)

The Contractor shall:

- (a) Comply with all requirements of the *Contract*, Cabonne Council's Work Health and Safety Policy and Manual, and all statutory requirements for Work, Health and Safety
- (b) Ensure that each of its subcontractors and Consultants comply in like manner
- (c) Demonstrate to the *Principal* whenever requested that requirements of the *Contract* and statutory requirements for Work, Health and Safety are being met

- (d) Prior to the commencement of work, provide the *Principal* with certification that safety requirements of the *Contract* and statutory requirements for Work, Health and Safety are capable of being met
- (e) If the period of the contract exceeds three months the *Contractor* is to provide the *Principal* with a monthly certification that requirements of the Contract and statutory requirements for Work, Health and Safety are being met
- (f) The *Contractor* is to submit to the *Superintendent* an Occupational Health and Safety Management Plan to ensure compliance with relevant legislation and responsible work practices are followed. The Work, Health and Safety Management Plan shall address, but not be limited to, the following issues:
  - Contractor WH & S policies and objectives
  - Defining responsibilities of personnel responsible for WH & S matters and their qualifications
  - Identifying and allocation of human, technical and financial resources adequate to meet the WH & S needs
  - Managing compliance with WH & S legislation regulations, standards and codes
  - Acquiring and disseminating WH & S information
  - Planning and conducting safety training, including induction for new employees
  - Developing and implementing emergency procedures
  - Assessing subcontractors' abilities to comply with WH & S requirements;
  - Ensuring compliance with safe working rules
  - Preparing work method statements
  - Verifying that work areas, work methods, materials, plant and equipment comply with safety legislation standard and codes
  - Quarantining unsafe work areas, materials, plant and equipment
  - Reporting incidents and accidents and collating accident and injury statements;
  - Investigating incidents and accidents and initiating corrective actions to eliminate or reduce risk
  - Rehabilitating injured employees.

The WH & S plan shall be submitted by the *Contractor* to the Superintendent within 7 days of acceptance of the tender and shall be used by the Superintendent to gain confidence that the *Contractor* has recognised and has the ability to meet the statutory requirements and will utilise responsible work practices.

Where inappropriate or inadequate provision of Work Health and Safety Management by the *Contractor* or Contractor's Subcontractor results in costs, losses or damages incurred by the *Principal* or claims by third parties against the *Principal* for either direct or consequential costs, losses or damages, the *Contractor* shall be liable for costs, losses or damages associated with any claim including but not limited to administration costs incurred by the *Principal* in resolving such claim.

#### CLAUSE 45. ENVIRONMENTAL SYSTEMS PLANNING

The Contractor shall:

- (a) Comply with all requirements of the *Contract* and statutory requirements for protection of the environment
- (b) Ensure that each of its subcontractors and *Consultants* comply in like manner
- (c) Demonstrate to the *Principal* by mutual inspection and/or documentation whenever requested that requirements of the *Contract* and statutory requirements for the protection of the environment are being met
- (d) Prior to the commencement of work, provide the *Principal* with certification that the requirements of the *Contract* and statutory requirements for the protection of the environment are capable of being met by the *Contractors'* organisation and management
- (e) If the period of the contract exceeds three months the *Contractor* is to provide the *Principal* with a monthly certification that the requirements of the *Contract* and statutory requirements for protecting the environment are being met
- (f) The *Contractor* is responsible for and must at its own cost make good any damage to the environment caused by the execution of the works.

Where inappropriate or inadequate provision of environmental management by the *Contractor* or subcontractor results in costs, losses or damages incurred by the *Principal* or claims by third parties against the *Principal* for either direct or consequential costs, losses or damages, the *Contractor* shall be liable for costs, losses or damages associated with any claim including but not limited to administration costs incurred by the *Principal* in resolving such claim.

#### CLAUSE 46. HOURS OF WORK

The hours of work under the Contract shall be limited to:

| 7.00am | το | 5.00pm | Mondays to Fridays |  |
|--------|----|--------|--------------------|--|
| 7.00am | to | 5.00pm | Saturdays          |  |

No Work Sundays or Public Holidays

If, in the interests of the safety or to protect life or property the *Contractor* finds it necessary to carry out, without the prior approval of the *Superintendent*, work outside the defined hours of work, the *Contractor* shall inform the *Superintendent* in writing of the circumstances within 24 hours. Extended hours shall be a mutual agreement between the Contractor and the Principal.

# **ANNEXURE - PART C**

#### **ANNEXURE PART C** STATUTORY DECLARATION

| Ι,       | (Full name of Declarant)  |                                      |  |
|----------|---|--------------------------------------|--|
| of       | (Address)   |                                      |  |
|          | do hereby solemnly declare and affirm tha   | ıt:                                  |  |
| 1.       | I am the representative of the Contractor:  |                                      | (Name of Contractor and ACN if applicable)   |
|          | in the Office Bearer capacity of:   |                                      | (Position Title of Declarant)  |
|          | the said Contractor having a contract for:  |                                      | (Name of Contract)   |
|          | with(Name of Principal)   |                                      | _ and I am in a position to know the facts attested to.  |
| 2.       | to them in respect of their employment of   | n wor                                | d by the Contractor have been paid all moneys due and payable k under the Contract, with the exception of the workers and the s & ADDRESSES OF WORKERS, THE AMOUNTS OWING, AND WHETHER IN C).  |
| 3.       | performance of work under the Contract a exception of the subcontractors and su   | and the                              | etor have been paid all moneys due and payable to them for the esupply of materials for use in work under the Contract, with the sand the respective amounts listed below: (INSERT NAMES & S, THE AMOUNTS OWING AND WHETHER IN RESPECT OF MATERIALS)   |
| 4.       | terms to this declaration that all workers,<br>have been paid all moneys due and pa<br>exception of the workers, subcontractors a<br>of anything to the contrary, and on the ba | subco<br>ayable<br>and su<br>asis of | contractor to the Contractor by Statutory Declaration in equivalent intractors, and suppliers engaged by them or their subcontractors to them in respect of their work under the Contract, with the uppliers and the respective amounts listed below. I am not aware the contents of the statutory declarations provided I believe that ESSES, THE AMOUNTS OWING AND WHETHER IN RESPECT OF WAGES |
|          |   |                                      | aid, according to the law in this behalf made, and subject to the  |
| punisnm  | nent by law provided for any wilfully false sta   | ateme                                | nt in any such declaration.  |
|          |   |                                      | (Signature of Declarant)   |
| Declared | d at:   | this                                 | (day month year)   |
| before n | (Signature of JP or authorised person)  |                                      |  |

Page 15 © IPWEA 2004



**CABONNE COUNCIL** 

### **CONTRACT No. 1160872**

#### **LUMP SUM CONTRACT**

for the

# INSTALLATION OF CULVERTS AND SUPPLY & INSTALL FOOTPATHS, KERB & GUTTERING IN THE CABONNE COUNCIL LGA

## **SPECIFICATIONS**

PREPARED BY:
COUNCIL'S DEPARTMENT OF
TRANSPORT INFRASTRUCTURE
DATE: SEPTEMBER 2020

#### **SPECIFICATION**

| CLAUS              | SE CONTENTS                                   | PAGE |
|--------------------|---|------|
| GENER              | RAL REQUIREMENTS                              | 4    |
| TS.01              | DEFINITIONS                                   | 4    |
| TS.02              | PROJECT DESCRIPTION                           | 4    |
| TS.03              | LOCATION OF THE PROJECT                       | 4    |
| TS.04              | SCOPE OF WORKS                                | 4    |
| TS.05              | SPECIFICATION DOCUMENTS                       | 5    |
| TS.06              | WORKING AREA                                  | 5    |
| TS.07              | ACCESS TO SITE                                | 5    |
| TS.08              | POSSESSION OF SITE                            | 5    |
| TS.09              | CONTRACTORS REPRESENTATIVE                    | 6    |
| TS.10              | PROJECT MEETINGS                              | 6    |
| TS.11              | LOCATING SERVICES                             | 6    |
| TS.12              | DAMAGE TO PUBLIC PROPERTY                     | 7    |
| TS.13              | MATERIALS SUPPLIED BY THE PRINCIPAL           | 7    |
| TS.14              | DELAYS DUE TO WET WEATHER AND FLOODING        | 7    |
| QUALI <sup>-</sup> | TY REQUIREMENTS                               | 7    |
| TS.15              | QUALITY SYSTEM                                | 7    |
| CONST              | TRUCTION REQUIREMENTS                         | 8    |
| TS.16              | GENERAL SITE CONSIDERATION                    | 8    |
| TS.17              | SITE CLEARING                                 | 8    |
| TS.18              | EARTHWORKS                                    | 8    |
| TS.19              | PROJECT COMPLETION                            | 8    |
| ENVIR              | ONMENTAL PROTECTION REQURIMENTS               | 9    |
| TS.20              | GENERAL ENVIRONMENTAL PROTECTION REQUIREMENTS | g    |
| TS.21              | STOCK PILE SITES                              | g    |
| TS.22              | DUMPING OF RUBBISH AND EXCESS MATERIAL        | 9    |

| Contract | No. 1160872                     | SPECIFICATION |  |
|----------|---------------------------------|---------------|--|
| TS.23    | RESTORATION OF DISTURBED GROUND | 10            |  |
| WORK     | HEALTH AND SAFETY REQUIREMENTS  | 10            |  |
| TS 24    | WORK HEALTH AND SAFETY          | 10            |  |

© IPWEA 2004 3

#### **GENERAL REQUIREMENTS**

#### TS.01 DEFINITIONS

- 1. The following definitions shall be used:
  - Project Manager Council appointed officer responsible for the management of the project.

#### **Definitions**

#### TS.02 PROJECT DESCRIPTION

1. The Contract involves the installation of culverts and supply & install footpaths, kerb & guttering anywhere within the Cabonne Council Local Government Area.

#### Description

#### TS.03 LOCATION OF THE PROJECT

- 1. The location of the project is:
  - Cabonne Council Local Government Area. Shown in the location map in Information for Tenderers: 1. Project Identification and Description.

#### Location

#### TS.04 SCOPE OF WORKS

- 1. The works are to include, but not be limited to, the following works:
- a) Preparation, boxing, supply, placement and finishing of concrete footpaths throughout the Cabonne Council Local Government Area

Scope of Works

- b) Preparation, boxing, supply, placement and finishing of concrete kerbs and guttering throughout the Cabonne Council Local Government Area
- c) Removal of existing footpaths before the construction of new footpaths throughout the Cabonne Council Local Government Area
- d) Removal of existing kerbs and guttering before the construction of new kerbs and guttering throughout the Cabonne Council Local Government Area
- e) Installation of pipes, boxes and headwalls to suit pipes and box culverts throughout the Cabonne Council Local Government Area

© IPWEA 2004 4

#### TS.05 SPECIFICATION DOCUMENTS

 All works under the contract shall be executed in accordance with relevant current Transport for New South Wales (TfNSW) Specification, Australian Standards, Council requirements and industry best practice, based on current documentation at date of calling for tender submissions. If there is discrepancy in the Standards, TfNSW specifications will take precedence.

Documents

#### TS.06 WORKING AREA

1. The working area available to the Contractor during construction of the works under this Contract is within the Cabonne Council LGA shown on the location map in Information for Tenderers: - 1. Project Identification and Description.

Working Area

- 2. If further clearing of the site is required, approval must be gained from the Principal.
- 3. If at any time the fences in the working area are damaged the Contractor will be responsible for any cost associated with damage restoration and or fines imposed.

Damage to Fences

#### TS.07 ACCESS TO SITE

1. The Contractor shall be responsible for the maintenance of roadways required on the worksite to undertake the work under the Contract.

Maintenance of roadways within site area

- 2. The Contractor shall be responsible for the safe movement of traffic and pedestrians into and out of the working area in accordance with TfNSW G10.
- Movement of traffic
- 3. The Contractor will be responsible for site inductions. All workers / people deemed necessary will be given a site induction and have their names added to the register, if required with the Contractors WH&S Management Plan.

Site inductions

#### TS.08 POSSESSION OF SITE

 The time for giving possession of site for establishment of the Contractor's facilities only is from the date of execution of the Formal Instrument of Agreement. Formal Instrument of Agreement

2. Possession shall be denied to the remainder of the site to allow for:

Possession to be withheld

© IPWEA 2004 5

- Submission of the Construction Programme
- Release of the Hold Point for the Project Work Health & Safety (WHS)
   Management Plan
- Release of the Hold Point for the Contractor's Environmental Management Plan and
- Submission of the Project Quality Plan.

#### TS.09 CONTRACTORS REPRESENTATIVE

 The Contractor shall provide a Representative on the site at all times during which any activities relating to the execution of the Works under the Contract are taking place and, if required by the Principal, at such other times and at such other places at or in which any activities relating to the execution of the Works under the Contract are taking place. Contractors Representativ

2. The Representative shall have a minimum of five years of proven and demonstrated contract management experience including programming of works and engagement and management of subcontractors.

Technical Requirement for Representativ

#### TS.10 PROJECT MEETINGS

- 1. The Project Manager and the Contractor shall hold a minuted meeting each fortnight, to cover such issues as
  - Progress in relation to the works program.

Agenda for meetings

- Any Project Manager directions to the Contractor
- · Other as required.
- 2. The Project Manager shall keep a written record of these meetings. A copy of the minutes shall be sent to all attendees.

Minutes of meeting

3. Where no meeting is held this, needs to be formally recorded along with the reasons for not holding the meeting.

#### TS.11 LOCATING SERVICES

 It is the Contractor's responsibility in Consultation with the relevant assets owners to locate all services. The Contractor is to contact "Dial Before You Dig" and other concerned asset owners to locate the services. Contractors responsibility

2. Council shall in no way be responsible for locating services on public or private property.

Council not liable

© IPWEA 2004 6

#### TS.12 DAMAGE TO PUBLIC PROPERTY

1. If during construction any public utility is damaged it is to be repaired by the appropriate authority at the Contractors cost.

Damage to Public Property

2. Where existing services must be interrupted to enable carrying out of the works such interruption shall be at a time agreed by the superintendent. Organise with the responsible servicing authority so that the interruption shall be for the minimum practical time. Give notices of the interruption to all the affected parties.

Interruption of Services

#### TS.13 MATERIALS SUPPLIED BY THE PRINCIPAL

1. Pipes, Boxes and Headwalls shall be supplied by the Principal.

Materials supplied by the Principal

## TS.14 DELAYS DUE TO WET WEATHER AND FLOODING

1. Notwithstanding anything to the contrary in the Contract, all costs arising from delays to the completion of the Works due to wet weather and its consequences shall be borne by the Contractor.

Wet weather days

2. The Contractor shall make every endeavour to reschedule construction activities to minimise all wet weather or flooding delays to the Works over the contract period. The Principal shall be entitled to take into account the Contractor's endeavours to mitigate such delays when assessing claims against extensions of time.

Mitigation of wet weather delays

3. Should the Pricipal direct a suspension of the whole or any part of the Works during prolonged flooding delays, the time of such suspension shall not qualify as "Excessive wet weather delay". Entitlement to payment in such circumstances shall be determined by the Superintendent.

Loss of time due to floodina

#### TS.15 QUALITY SYSTEM

1. The Contractor shall plan, establish, document and maintain a Quality System, which conforms to the requirements of the Contract access to the Contractor's and Sub Contractor's quality systems for monitoring and quality auditing the quality system.

Required

2. The Quality System proposed by the Contractor and Sub Contractors shall be used as an aid to achieve compliance with the requirements of the Contract and to document such compliance

Manual to Support Contract Requirements

© IPWEA 2004 7

#### **CONSTRUCTION REQUIREMENTS**

#### TS.16 GENERAL SITE CONSIDERATION

#### 1. Time for Completion

 The works under the contract are for the fiscal year 2020-21. The works may be spread over the Council area. The time for practical completion of the works at each site will be negotiated at the time of acceptance of the offer.

Contract Period

#### TS.17 SITE CLEARING

1. The Contractor shall remove everything on or above the site surface including rubbish, scrap, grass, vegetable matter and organic debris, scrub, trees, timber, stumps, boulders and rubble.

Clearing and grubbing

2. The Contractor shall remove cleared and grubbed material from the site.

Disposal of material

#### TS.18 EARTHWORKS

 The Contractor shall carry out all excavation works necessary to allow the construction of the new works at his own expense. The Contractor shall arrange and bear all costs and charges required for compliance with any Authority having jurisdiction over the works for such aspects as disconnection of services, temporary services and continuation of supply.

General required

#### TS.19 PROJECT COMPLETION

#### 1. Site Clean Up

- On completion of all work all excess materials and soils must be removed from the site to the satisfaction of the Principal.
- All disturbed grass areas to be reinstated to the satisfaction of the Principal.

Site clean up

- All temporary fences and signage to be removed and any damaged areas to be made good.
- All damaged areas must be repaired to the same condition or better as they

© IPWEA 2004 8

Contract No. 1160872 SPECIFICATION

were prior to the works commencing and to the Principal's satisfaction.

#### 2. Practical Completion

The Contractor is to apply for a certificate of practical completion no later than
 14 days prior to the expected date of practical completion.

Certificate of practical completion

- Prior to practical completion being awarded the Principal and the Contractor are to conduct a joint site inspection to determine if all works as per the approved design and specifications are completed.
- If completed works are not satisfactory, then the Contractor will be issued notice under the contract works, stating the non-compliant items and be given 14 days to complete or rectify the works as appropriate.

#### **ENVIRONMENTAL PROTECTION REQUIREMENTS**

# TS.20 GENERAL ENVIRONMENTAL PROTECTION REQUIREMENTS

1. The Contractor shall be responsible for ensuring that all works comply with all relevant regulations relating to the protection of the environment.

Contractors responsibilitie

#### TS.21 STOCK PILE SITES

1. The Contractor shall ensure that stockpile sites are not located in or near areas susceptible to overland runoff such as creeks and gullies.

Location of stockpile

2. No material shall be stockpiled on public land without the approval of the Project Manager.

Stockpiles on Public Land

# TS.22 DUMPING OF RUBBISH AND EXCESS MATERIAL

 All debris and excess material from the works shall be transported to the approved landfill site. Dumping of rubbish

2. No debris or excess material shall be dumped on private property without the approval of the Project Manager.

Approval of Project Manager

© IPWEA 2004 9

**CABONNE COUNCIL** 

Contract No. 1160872 SPECIFICATION

#### TS.23 RESTORATION OF DISTURBED GROUND

1. The Contractor shall restore all ground disturbed by the works to a standard similar or better than that prior to the commencement of the work.

General required

2. The Contractor is to ensure that settlement of backfill in trenches and other areas is minimised and is responsible for filling any sunken areas.

Settlement of trenches

3. On completion of the project, the site office and any security fencing must be totally removed. If the site office is on private property, the Contractor will need to obtain from the property owner a letter indicating that they are satisfied with the condition that the site has been left in.

Removal of site office

Project Manager as final arbiter

4. The Project Manager shall be the final arbiter of the quality of the restoration.

#### **WORK HEALTH AND SAFETY REQUIREMENTS**

#### TS.24 WORK HEALTH AND SAFETY

- 1. The following Safety Standards shall apply for the Works:
  - Work Health and Safety Act 2011 and relevant Codes and Regulations.
  - Work Health and Safety Regulations 2017 & related Codes and Practice as well as:
    - a) The Contractor shall implement a training program for all personnel working on the Works under this Contract, including any Sub Contractors personnel, and satisfy the requirements of Occupational Health and Safety legislation.

General requirements

- The Contractor must ensure that all personnel and Sub Contractors engaged on activities associated with the project adopt safe work practices
- c) The Contractor must ensure that the Sub Contractors fulfils all requirements of the Work Health and Safety Act and all relevant [State] Work cover Authority Regulations. The Contractor shall ensure that work is carried out in a safe manner for the safety of the work force and general public alike. The Contractor must detail how WH&S issues and training will be handled during the construction of the Works.
- The Contractor must comply with and ensure that it's employees, subcontractors and agents comply with any Acts, regulations, local laws and by-laws, Codes of Practice, Australian Standards, Councils' WH & S document, policies and procedures, which are in any way applicable to this contract or the performance of

Legislation

© IPWEA 2004 10

**CABONNE COUNCIL** 

Contract No. 1160872 SPECIFICATION

the services under this contract.

3. The Contractor shall prepare and implement a Project Work Health and Safety Management Plan.

WHS Plan

4. It is a policy of Council that all Contractors, Sub Contractors, Consultants and agents who undertake works for or on behalf of Council comply with the requirements of the Cabonne Council WH&S Manual and Policies.

Council WH&S Handbook

5. All Contractor and Sub-Contractor employees will be required to attend a CENTROC WHS induction prior to the commencement of the works. Employees who have completed the CENTROC induction since 2014 are not required to redo. Employees will need to provide proof of attendance.

CENTROC Induction

© IPWEA 2004 11

**CABONNE COUNCIL** 



#### **CABONNE COUNCIL**

# CONTRACT No. 1160872 LUMP SUM CONTRACT

for the

# INSTALLATION OF CULVERTS AND SUPPLY & INSTALL FOOTPATHS, KERB & GUTTERING IN THE CABONNE COUNCIL LGA

# **TENDER SUBMISSION DOCUMENTS**

PREPARED BY:
COUNCIL'S DEPARTMENT OF
TRANSPORT INFRASTRUCTURE
DATE: SEPTEMBER 2020

#### NOMINATION OF REQUIRED TENDER SUBMISSIONS

All Submitted information will be treated as confidential

#### **TENDER FORMS AND DECLARATIONS**

- 1. Tender Form
- 2. Lump Sum Tender Form
- 3. Bill of Quantities
- 4. Tenderer's Particulars Personnel
- 5. Register of Tenderer's Subcontractors and Suppliers
- 6. Major Machinery and Equipment
- 7. Statutory Declaration on Non-Collusive Tender Submission
- 8. Acquaintance with Site
- 9. Receipt of Addenda
- 10. Statement of Conformance

#### INSTRUCTION TO TENDERER

The Tenderer shall complete in full and submit the forms in numerical order listed above. The completed forms, declarations and required information shall comprise the Tender Submission Documents. Initial and date each form at the bottom right hand side of each page.

#### **COMPLETION OF DOCUMENTS**

The omission of / failure to complete the forms listed above may, at the absolute discretion of the Principal, result in a nonconforming tender and be subject to rejection.

#### **TENDERER'S ACKNOWLEDGMENT**

| Contract: Installation of Culverts and | Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |
|--|---|
| <b>Contract No</b> : 1160872           |   |
| Date:                                  |   |
| Signature of Tenderer:                 |   |

#### **TENDER SUBMISSION FORM 1**

# **TENDER FORM**

|                      | The Tenderer must complete and submit with Tender sub<br>All Submitted information will be treated as confident |                                  |
|----------------------|---|----------------------------------|
| l,                   |   | (Print name)                     |
| of                   |   |                                  |
|                      |   | (Address)                        |
| on this              | day of  | , Year                           |
|                      | uainted myself with the Conditions of Tender and he Contract do hereby tender to perform the work descri        |                                  |
| Contract: Installati | ion of Culverts and Supply & Install Footpaths, Kerb & Gut  | ering in the Cabonne Council LGA |
| Contract No: 1160    | 0872  |                                  |
| as invited by: CAB   | ONNE COUNCIL, in accordance with the following docu   | ments.                           |
| Condition            | ns of Contract  |                                  |
| Informati            | on for Tenderers  |                                  |
| Specifica            | itions  |                                  |
| Drawings             | S   |                                  |
| Tender S             | Submission Documents+   |                                  |
| Addendu              | ım (if any)   |                                  |
|                      |   |                                  |

By submitting this Tender, the Tenderer warrants and represents that the Tenderer has made their own enquiries and investigations and has obtained professional advice and all other relevant information so as to inform itself of all risks and contingencies which may affect the Tender price. The Tenderer warrants and represents that it has included for all such risks and contingencies in the Submission.

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |  |
|-----------------|--|----------------------------|--|--|
| Contract Number | 1160872 Tenderer to Complete   |                            |  |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |  |

# **TENDER SUBMISSION FORM 1 continued**

| Signature of Tenderer:         |          |              |
|--------------------------------|----------|--------------|
| Phone and facsimile numbers: _ |          |              |
| Subscribed and declared this:  | Day of   | Year         |
| Before me:                     |          | (Print name) |
| Witness:                       |          | (Signature)  |
| Referees                       |          |              |
| Name                           | Position | Telephone No |
| 1                              |          |              |
|                                |          |              |
|                                |          |              |
| 2                              |          |              |
|                                |          |              |
|                                |          |              |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |  |
|-----------------|--|----------------------------|--|--|
| Contract Number | 1160872 Tenderer to Complete   |                            |  |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |  |

#### **TENDER SUBMISSION FORM 2**

#### **LUMP SUM TENDER FORM**

The Tenderer must complete and submit with tender. All Submitted information will be treated as confidential

The Tenderer shall complete all or part of the following information in accordance with their Tender Submission. Amounts specified for these Lump Sum amount shall equal the extended totals from the relevant Bill of Quantities.

**Description** 

**Lump Sum Amount** 

(including GST)

All amounts shall be inclusive of GST.

Tender

Submission

**Form** 

| 3               | All Works under Contract |             |        |              |
|-----------------|--------------------------|-------------|--------|--------------|
| Signature of Te | nderer:                  |             |        |              |
| Phone Number    | :                        | Fax Number: |        |              |
| Subscribed and  | I declared this: Day of  |             | (Year) |              |
| Before me:      |                          |             |        | (Print name) |
| Witness:        |                          |             |        | (Signature)  |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                      |  |  |
|-----------------|--|----------------------|--|--|
| Contract Number | 1160872  | Tenderer to Complete |  |  |
| Council         | Cabonne Council  | Tenderer's Initial   |  |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date                 |  |  |

# **TENDER SUBMISSION FORM 3**

# **BILL OF QUANTITIES – ALL WORKS UNDER CONTRACT**

1. The quantities shown are estimated quantities only and are not to be taken as correct quantities of work to be carried out.

2. All prices and rates shall be GST inclusive.

| ITEM | DESCRIPTION | UNIT | QTY | RATE | AMOUNT |
|------|-------------|------|-----|------|--------|
|      |             |      |     |      |        |

|    | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council Local Government Area |      |     |  |  |
|----|--|------|-----|--|--|
| 1  | Supply and Install Footpath 2.5m Shared Pathway  | m²   | 500 |  |  |
| 2  | Supply and Install Kerb and Guttering  | m    | 250 |  |  |
| 3  | Pipes (RCP) Installation Only – 375mm  | Item | 6   |  |  |
| 4  | Pipes (RCP) Installation Only – 450mm  | ltem | 6   |  |  |
| 5  | Pipes (RCP) Installation Only – 600mm  | Item | 6   |  |  |
| 6  | Pipes (RCP) Installation Only – 750mm  | Item | 6   |  |  |
| 7  | Pipes (RCP) Installation Only – 900mm  | Item | 6   |  |  |
| 8  | Headwalls to suit (RCP) Installation Only – 375mm  | Item | 6   |  |  |
| 9  | Headwalls to suit (RCP) Installation Only – 450mm  | Item | 6   |  |  |
| 10 | Headwalls to suit (RCP) Installation Only – 600mm  | Item | 6   |  |  |
| 11 | Headwalls to suit (RCP) Installation Only – 750mm  | Item | 6   |  |  |
| 12 | Headwalls to suit (RCP) Installation Only – 900mm  | Item | 6   |  |  |
| 13 | Boxes (RCBC) Installation Only – 300 x 225   | Item | 6   |  |  |
| 14 | Boxes (RCBC) Installation Only – 450 x 300   | Item | 6   |  |  |
| 15 | Boxes (RCBC) Installation Only – 600 x 300   | Item | 6   |  |  |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |  |
|-----------------|--|----------------------------|--|--|
| Contract Number | 1160872 Tenderer to Complete   |                            |  |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |  |

| 16 | Boxes (RCBC) Installation Only – 600 x 450  | Item         | 6      |                |  |
|----|---|--------------|--------|----------------|--|
| 17 | Boxes (RCBC) Installation Only – 900 x 300  | Item         | 6      |                |  |
| 18 | Headwalls to suit Box Culverts (RCBC) Installation Only – 300 x 225   | Item         | 6      |                |  |
| 19 | Headwalls to suit Box Culverts (RCBC) Installation Only – 450 x 300   | Item         | 6      |                |  |
| 20 | Headwalls to suit Box Culverts (RCBC) Installation Only – 600 x 300   | Item         | 6      |                |  |
| 21 | Headwalls to suit Box Culverts (RCBC) Installation Only – 600 x 450   | Item         | 6      |                |  |
| 22 | Headwalls to suit Box Culverts (RCBC) Installation Only – 900 x 600   | Item         | 6      |                |  |
| 23 | All Other Works under the Contract not included elsewhere in accordance with the Drawings and Specifications (Provide Break Up) | Lump<br>Sump |        |                |  |
|    |   | •            | Subtot | al (Excl. GST) |  |
|    | GST   |              |        |                |  |
|    | TOTAL LUMP SUM CONTRACT PRICE (Incl. GST)   |              |        |                |  |

#### Note:

Cabonne Council to supply traffic control

Cabonne Council to supply pipes / box culverts and headwalls

Contractor to install pipes / box culverts and headwalls

Contractor to supply and install kerb & guttering and footpaths

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |  |
|-----------------|--|----------------------------|--|--|
| Contract Number | 1160872 Tenderer to Complete   |                            |  |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |  |

# **TENDER SUBMISSION FORM 4**

#### **TENDERER'S PARTICULARS - PERSONNEL**

The Tenderer must complete and submit with tender All Submitted information will be treated as confidential

Provide the names of the Project Manager and Site Manager or Responsible Officer in the event of a winning tender.

| esponsibilities for this Project:  tractor Site Manager  Name  Company Role  Estimate Commits | ment (%) | Years Exp  Years Exp  In current firm | prior           |
|---|----------|---------------------------------------|-----------------|
| Commitr   |          |                                       |                 |
| Name Company Role Estimate Commits  |          |                                       |                 |
| Name Company Role Estimate Commits  |          |                                       |                 |
| Commitr   |          |                                       |                 |
| responsibilities for this Project:  |          |                                       |                 |
|   |          |                                       |                 |
|   |          |                                       |                 |
| ign Sub Contractor  |          |                                       |                 |
| Name Company Role Estimate Commitr  |          | Years Exp                             | erience<br>prio |
|   |          |                                       |                 |
| responsibilities for this Project:  |          |                                       |                 |
|   |          |                                       |                 |
|   |          |                                       |                 |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |
|-----------------|--|----------------------------|--|
| Contract Number | Tenderer to Complete   |                            |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |

# **TENDER SUBMISSION FORM 5**

# **REGISTER OF TENDERER'S SUBCONTRACTORS AND SUPPLIERS**

The Contractor must complete and submit with Tender submission All Submitted information will be treated as confidential

The Tenderer is instructed to compile a listing below of all Selected Subcontractors and Suppliers which the Tenderer expects to use to execute the Works under the terms of this Contract.

| Supplier or Contractor | Telephone No. | Description of work or materials |
|------------------------|---------------|----------------------------------|
| 1.                     |               |                                  |
| 2.                     |               |                                  |
| 3.                     |               |                                  |
| 4.                     |               |                                  |
| 5.                     |               |                                  |
| 6.                     |               |                                  |
| 7.                     |               |                                  |
| 8.                     |               |                                  |
| 9.                     |               |                                  |
| 10.                    |               |                                  |
| 11.                    |               |                                  |
| 12.                    |               |                                  |
| 13.                    |               |                                  |
| 14.                    |               |                                  |
| 15.                    |               |                                  |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |  |  |
|-----------------|--|--|--|
| Contract Number | 160872 Tenderer to Complete  |  |  |
| Council         | Cabonne Council  | Tenderer's Initial   |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | O noon Wednesday, 14 October 2020 Date Submitted by Tenderer |  |

# **TENDER SUBMISSION FORM 6**

#### **MAJOR MACHINERY AND EQUIPMENT**

The Tenderer must complete and submit with Tender submission All Submitted information will be treated as confidential

The Tenderer is instructed to compile a listing below of all Major Equipment and Machinery proposed to execute the Works under the terms of this Contract.

| Make / Model | Description | Year of<br>Manufacture | Owned or<br>Leased |
|--------------|-------------|------------------------|--------------------|
| 1.           |             |                        |                    |
| 2.           |             |                        |                    |
| 3.           |             |                        |                    |
| 4.           |             |                        |                    |
| 5.           |             |                        |                    |
| 6.           |             |                        |                    |
| 7.           |             |                        |                    |
| 8.           |             |                        |                    |
| 9.           |             |                        |                    |
| 10.          |             |                        |                    |
| 11.          |             |                        |                    |
| 12.          |             |                        |                    |
| 13.          |             |                        |                    |
| 14.          |             |                        |                    |
| 15.          |             |                        |                    |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |
|-----------------|--|----------------------------|--|
| Contract Number | Tenderer to Complete   |                            |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |

# **TENDER SUBMISSION FORM 7**

# STATUTORY DECLARATION ON NON-COLLUSIVE TENDER DECLARATION

The Tenderer must complete and submit with Tender submission All Submitted information will be treated as confidential

| I, _ |   |   | (Print name),   |
|------|---|---|---|
| of   |   |   | (Address),  |
| do   | nereby solemnly declare and affirm the follo  | ing;  |   |
| 1.   | I, after having made due inquiry believe the  | following to be completely accurate to the best of my k   | knowledge.  |
| 2.   | Neither the Tenderer nor the Tenderers A kind to a representative of the Principal in the second sec | ents or Servants have entered into any contract or ag<br>le event of a winning tender.  | reement to offer payment of any                                     |
| 3.   |   | gents or Servants have had any knowledge of the page price of the enclosed tender to any external source  |   |
| 4.   | Neither the Tenderer nor the Tenderers A kind to an unsuccessful Tenderer in the ev   | ents or Servants have entered into any contract or agent of a winning submission.   | reement to offer payment of any                                     |
| 5.   | The Tenderer is not aware of any facts<br>Tenderer attempted to acquire information<br>or their Representative's Agents or Servar   | hich would affect the decision of the Principal in acrelevant to the Tenderer award process by soliciting the state of the Tenderer award process by the state of the tenderer award process by the state of the tenderer award process by the state of the state of the tenderer award process by the state of the tenderer award process by the state of the state | cepting the Tender nor has the<br>the Principal, the Superintendent |
| 6.   | Neither the Tenderer nor the Tenderers A which results in a payment of unsuccessful   | ents or Servants have entered into any agreement wi<br>Tender fees.   | ith other Tenderers or third party                                  |
| 7.   | The contents of this document are true ar any form.   | d correct to the best of my knowledge and in no way ha  | ave been written under duress of                                    |
|      | ake this solemn declaration as to the matte<br>provided for any wilfully false statement in a   | aforesaid, according to the law in this behalf made, and such declaration.  | nd subject to the punishment by                                     |
| Siç  | nature of Tenderer:   |   |   |
| Su   | bscribed and declared at:   |   |   |
|      |   | Year  |   |
| Ве   | fore me:  |   | (Print name)  |
| Wi   | ness:   |   | (Signature)   |
| (Ju  | tice of the Peace or authorised person)   |   |   |
|      |   |   |   |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |
|-----------------|--|----------------------------|--|
| Contract Number | 1160872 Tenderer to Complete   |                            |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |

# **TENDER SUBMISSION FORM 8**

# **ACQUAINTANCE WITH SITE**

The Tenderer must complete and submit with tender All Submitted information will be treated as confidential

This form shall be signed by the Tenderer as a guarantee to the Principal that the Tenderer has undertaken a site inspection without direction of the Principal so as to be fully acquainted with the physical characteristics of the site.

Site Description: Cabonne Council LGA

#### **DECLARATION OF SITE INSPECTION**

| I,                                   | , of the Tendering Organisation   |
|--------------------------------------|---|
| sound knowledge<br>that may arise as | accord, conducted an inspection of the aforementioned site and in doing so I have acquired as of the physical characteristics of the site and any consequential procedures and processes a result of any environmental or geographical constraints or conditions and in doing so have onal, State, and Council regulations, legislation and bylaws. |
|                                      | derstands that it is the responsibility of the Tendering Organisation to inform all personnel contractors of the Tendering Organisation of all information pursuant to the preceding  |
| Name:                                |   |
| Signature:                           |   |
| Date:                                |   |
|                                      |   |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |
|-----------------|--|----------------------------|--|
| Contract Number | 1160872  | Tenderer to Complete       |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |

# **TENDER SUBMISSION FORM 9**

# **RECEIPT OF ADDENDA**

The Tenderer must complete and submit with tender All Submitted information will be treated as confidential

The Tenderer is to acknowledge that it received the addenda listed below during the tender period and that the tender has been prepared having regard to these addenda.

| Addenda No. | Brief Description<br>(eg. Specification Page No, Clause No, Schedule<br>No) | Date Received |
|-------------|---|---------------|
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |
|             |   |               |

This Tender has been prepared having regard to the addenda listed above.

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |
|-----------------|--|----------------------------|--|
| Contract Number | 1160872  | Tenderer to Complete       |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |

#### **TENDER SUBMISSION FORM 10**

#### STATEMENT OF CONFORMANCE

The Tenderer must complete and submit with tender All Submitted information will be treated as confidential

The Tenderer is to signify whether or not the submitted Tender conforms with the requirements of the Tender Documents by striking out below \*\* that which is not applicable.

This Tender \*\* does / does not \*\* conform.

Should the Tender not conform with the requirements of the Tender Documents, the Tenderer shall list below all areas of non-conformance and the reasons for such non-conformance and shall value \* each such non-conformance so that in the event of the non-conformance being deemed unacceptable, the Contract sum can be adjusted accordingly. If the non-conformances are not priced and are deemed to be unacceptable, the tender may not be further considered.

| Area of Non-Conformance and Reason | * Value of<br>Non-Conformance<br>(\$) |
|------------------------------------|---------------------------------------|
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |
|                                    |                                       |

| Contract        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |                            |  |  |
|-----------------|--|----------------------------|--|--|
| Contract Number | 1160872  | Tenderer to Complete       |  |  |
| Council         | Cabonne Council  | Tenderer's Initial         |  |  |
| Submission Date | 12.00 noon Wednesday, 14 October 2020  | Date Submitted by Tenderer |  |  |

# **INSTRUMENT OF AGREEMENT**

This instrument shall be completed by Principal and Contractor after acceptance of the tender. It is included here for the Tenderer's information.

| This form con    | nprises a binding  | Contractual Agreement  | between:  |            |  |  |
|------------------|--|--|---|------------|--|--|
| CABONNE CO       | OUNCIL (Principal)   | and  | (Contracto  | r)         |  |  |
| to faithfully ex | recute the whole o   | of the Works as set out in   | n the documents below for the   |            |  |  |
| Contract:        | Installation of Culverts and Supply & Install Footpaths, Kerb & Guttering in the Cabonne Council LGA |  |   |            |  |  |
| Contract No:     | 1160872  |  |   |            |  |  |
| Within the Are   | ea of Cabonne Co   | uncil  |   |            |  |  |
| in accordance    | e with: Tenderers  | s' Tender dated  | and   |            |  |  |
|                  | Letter of A  | Acceptance dated   |   |            |  |  |
|                  |  | Contractual Documen  | t Parts Include   |            |  |  |
|                  |  | The General Conditions of Contract AS 4000-1997 Annexure to the General Conditions of Contract |   |            |  |  |
| Specifi          | cations  |  |   |            |  |  |
| Drawin           | gs   |  |   |            |  |  |
| Tender           | Submission Documer   | nts  |   |            |  |  |
| Adden            | dums (if any)  |  |   |            |  |  |
| the Tenderer is  |  | of the tender is accurate o  | d as additional to the Contract Document<br>r complete and the Tenderer must make |            |  |  |
| Name of Cont     | ractor:  |  |   |            |  |  |
| Signature of C   | Contractor:  |  | Date:   |            |  |  |
| Address:         |  |  |   |            |  |  |
| Witness:         |  |  | (5  | Signature) |  |  |
| Signed for and   | on behalf of Cabor   | nne Council.   |   |            |  |  |
| General Mana     | nger   |  | Witness   | •••••      |  |  |
| Name of Gene     | eral Manager (prin   | t)   | Name of Witness (print)   |            |  |  |
| Date             |  |  | Date  |            |  |  |
